

GIBELO

2024 -03- 2 2

CONTROLLED CAR PRAISA PROJECT

GIBELO




# SELF INSPECTION SHEET

## CONFIDENTIAL INFORMATION




This document and the information contemplated therein have to be considered as Confidential Information pursuant to the provisions of Clause 25 of the MSA, and treated as such.


## APPLICATION REFERENCE









| MOUNTING                 | DESCRIPTION   | STATION                                   | CAR TYPE |    |    |                                     |    |     | WORK INSTRUCTION | SAFETY ?  |
|--------------------------|---------------|---|----------|----|----|-------------------------------------|----|-----|------------------|---|
|                          |               |   | TC1      | M4 | M1 | M2                                  | M3 | TC2 |                  |   |
| <input type="checkbox"/> | DTR3-PROCE-14 | LEVELLING, WEIGHTING AND BALANCING M CAR  | FT1140   | 1  | 1  | <input checked="" type="checkbox"/> | 1  |     | PRA.FT1140.04    | YES   |
| <input type="checkbox"/> | DTR3-PROCE-14 | LEVELLING, WEIGHTING AND BALANCING TC CAR | FT1140   | 1  |    |                                     |    | 1   | PRA.FT1140.05    | YES   |
| <input type="checkbox"/> | DTR3-PROCE-17 | LEVELLING, WEIGHTING AND BALANCING TC CAR | FT1140   | 1  | 1  | 1                                   | 1  | 1   | PRA.FT1140.05    | YES   |
| <input type="checkbox"/> | DTR3-PROCE-17 | LEVELLING, WEIGHTING AND BALANCING TC CAR | FT1140   | 1  | 1  | 1                                   | 1  | 1   | PRA.FT1140.05    | YES   |
| <input type="checkbox"/> |               |   |          |    |    |                                     |    |     |                  |   |
| <input type="checkbox"/> |               |   |          |    |    |                                     |    |     |                  |   |
| <input type="checkbox"/> |               |   |          |    |    |                                     |    |     |                  |   |


| REV | DATE      | MODIFICATION CONTENT  | RESPONSIBLE | NAME                 | DATE      |
|-----|-----------|---|-------------|----------------------|-----------|
| 7   | 2/11/2020 | UPDATE OF AIR TIGHTNESS TEST TIME FROM 4 MIN TO 5 MIN.<br>ADD PANTOGRAPH AIR TIGHTNESS. | APPROVER    | GIVEN SILOWA         | 2/11/2020 |
|     |           |   | CHECKER     | SIMON MOKOENA        | 2/11/2020 |
|     |           |   | COMPILER    | COMFORT MALATI       | 2/11/2020 |
| 8   | 9/13/2021 | ADDING GAUGE MEASUREMENT CHECK ON THE SI.   | APPROVER    | MAKOFANE LUCY        | 9/13/2021 |
|     |           |   | CHECKER     | RATAU EDISON         | 9/13/2021 |
|     |           |   | COMPILER    | TSAKANI KHOSA        | 9/13/2021 |
| 9   | 5/31/2022 | pressure valve (APV) Isolation  | APPROVER    | MAKHURUPETJI THABANG | 5/31/2022 |
|     |           |   | CHECKER     | HAZEL MGIBA          | 5/31/2022 |
|     |           |   | COMPILER    | RATAU EDISON         | 5/31/2021 |












| TUE   | CAR | OPERATOR NAME | DATE     | SELF INSPECTION NUMBER | PAGES |
|-------|-----|---------------|----------|------------------------|-------|
| TS215 | MC  | Khumyana      | 22/03/24 | SI.FT1140.52           | 01/08 |


|   |   |                        |  |                   |              |  |          |        |    |                |
|---|---|------------------------|--|-------------------|--------------|--|----------|--------|----|----------------|
|    | <h1>SELF INSPECTION<br/>INDUSTRIAL QUALITY</h1> |                        | Rev:09   | Project:<br>PRASA | SI.FT1140.52 |  |          |        |    |                |
|   |   |                        | Date:  |                   |              |  |          |        |    |                |
|   |   |                        | 5/31/2022                                      |                   |              |  |          |        |    |                |
| Cur:  | NCR:  | Work Station<br>FT1140 |  |                   |              |  |          |        |    |                |
|  Safety Related                          |   |                        |  |                   |              |  |          |        |    |                |
| I - Document and Instrument Control   |   |                        |  |                   |              |  |          |        |    |                |
| I.1 - Documents control   |   |                        |  |                   |              |  |          |        |    |                |
| Document  | TC1   | M1                     | M2   | M3                | M4           | TC2  | Revision | Remark | OK | Signature/Date |
| PRA.FT1140.04   |   |                        |  |                   |              |  |          |        |    |                |
| PRA.FT1140.05   |   |                        | X  |                   |              |  |          |        | ✓  | MCA 22/03/24   |
| PRA.FT1140.05   |   |                        |  |                   |              |  |          |        |    |                |
| I.2 - Instruments Control - Monitoring and Measuring Instrument Control (Used for all Instrument with calibration needed) |   |                        |  |                   |              |  |          |        |    |                |
| Instruments description   | Serial number                                   |                        | Calibration or Verification<br>Validation Date |                   | OK           | Signature/Date   |          |        |    |                |
| Mearing Tape  | GIBTA 0281                                      |                        | 23/01/23-23/01/24                              |                   | ✓            |  |          |        |    |                |
| Vernier Calliper  | GIBVR 0050                                      |                        | 21/11/23-21/11/24                              |                   | ✓            |  |          |        |    |                |
| Torque Wrench 320N.m  | A9630053  |                        | 21/08/23-21/08/24                              |                   | ✓            | <br>22/03/24 |          |        |    |                |
| Torque Wrench 150N.m  | B721TS66  |                        | 01/08/23-01/08/24                              |                   | ✓            |  |          |        |    |                |
| Torque Wrench 35N.m   | D2511023  |                        | 01/08/23-01/08/24                              |                   | ✓            |  |          |        |    |                |
|   |   |                        |  |                   |              |  |          |        |    |                |
|   |   |                        |  |                   |              |  |          |        |    |                |



|  | <h1>SELF INSPECTION<br/>INDUSTRIAL QUALITY</h1>                                     |  | Rev:09  | Project:<br>PRASA     | SI.FT1140.52   |         |     |  |  |  |  |   |          |
|---|---|--|---|-----------------------|----------------|---------|-----|--|--|--|--|---|----------|
|   |   |  | Date:   |                       |                |         |     |  |  |  |  |   |          |
|   |   |  | 5/31/2022   |                       |                |         |     |  |  |  |  |   |          |
| <b>II - Self Inspection - Items to Check</b>                                      |   |  |   |                       |                |         |     |  |  |  |  |   |          |
| <b>II.1 - Items to Check</b>  |   |  |   |                       |                |         |     |  |  |  |  |   |          |
| Item  | Picture/Sketch  | Description  | Criteria/Record   | OK                    | Signature/Date |         |     |  |  |  |  |   |          |
| 01  |    | Ensure that the average pressure valve (APV) is isolated by capping the two input pipes at the fittings installing the blanking fitting on the pipes highlighted                   |   | ✓                     | 22/03/24       |         |     |  |  |  |  |   |          |
| 02  |   | Check underframe pipe system Air tightness.<br>Test performance according to WI PRA FT1130.15.   | The test was performed and no leak was observed.<br>Initial pressure (IP): 104.9 bar<br>Final pressure (FP): 103.3 bar<br>FP - IP = 0,01 bar<br>APPROVAL CRITERIA: After 5 minutes the pressure cannot drops more than 0,2 bar      | ✓                     | 22/03/24       |         |     |  |  |  |  |   |          |
| 03  |    | Movement performed at least 50m to shudder the car. And position on the leveled load cell, with wheels on the center.  |   | ✓                     | 22/03/24       |         |     |  |  |  |  |   |          |
| 04  |  | Measurement inspection was done with car on condition AWO and the rail leveled.<br>(The load cells system must be leveled and calibrated)  | Calibration Validation Date<br>17/12/23   | ✓                     | 22/03/24       |         |     |  |  |  |  |   |          |
| 05  |  | In case of the equipments not installed, equivalent weight of the item should be added in the same place to simulate the equipment.<br>(Any simulated weight, add on pending list) | <table border="1"> <thead> <tr> <th>EQUIPMENT DESCRIPTION</th> <th>WEIGHT (kg)</th> </tr> </thead> <tbody> <tr> <td>gangway</td> <td>360</td> </tr> <tr> <td></td> <td></td> </tr> <tr> <td></td> <td></td> </tr> </tbody> </table> | EQUIPMENT DESCRIPTION | WEIGHT (kg)    | gangway | 360 |  |  |  |  | ✓ | 22/03/24 |
| EQUIPMENT DESCRIPTION   | WEIGHT (kg)   |  |   |                       |                |         |     |  |  |  |  |   |          |
| gangway   | 360   |  |   |                       |                |         |     |  |  |  |  |   |          |
|   |   |  |   |                       |                |         |     |  |  |  |  |   |          |
|   |   |  |   |                       |                |         |     |  |  |  |  |   |          |
| 06  |  | The pressure difference between air spring on each bogie when raise the pressure was maintained < 0.3 bar.   |   | ✓                     | 22/03/24       |         |     |  |  |  |  |   |          |
| 07  |  | Measurement recorded with empty suspension and loaded are on conformity with tolerances of the project   |   | ✓                     | 22/03/24       |         |     |  |  |  |  |   |          |
| 08  |  | All leveling measurements are according to the reference.<br>(Values out of reference must be recorded on "Description of defects")  |   | ✓                     | 22/03/24       |         |     |  |  |  |  |   |          |

  
 2024 -03- 2 2  
**CONTROLLED COPY**

|  |   | <b>SELF INSPECTION<br/>INDUSTRIAL QUALITY</b>   |   | Rev:09                 | Project:<br>PRASA | SI.FT1140.52    |
|---|---|---|---|------------------------|-------------------|-----------------|
|   |   |   |   | Date:<br><br>5/31/2022 |                   |                 |
| Item  | Picture/Sketch  | Description   | Criteria/Record   | OK                     | NO                | Signature/Date  |
| 09  |    | Check that the leveling rods are torqued and have torque marker.  |   | ✓                      |                   | MOR<br>22/03/24 |
| 10  |    | The difference of weight between the left and right wheels of each axis, must be ≤ 4%.<br>(Verify on the T&C equipment if all arrows are in green). |   | ✓                      |                   | MOR<br>22/03/24 |
| 11  |    | Remove the car, move back onto the load cells and repeat the step 09. Confirm if both are in the tolerance of ≤ 4%.                                 |   | ✓                      |                   | MOR<br>22/03/24 |
| 12  |    | 1 - Record shims thickness used on rod.<br>2 - All screws were torqued and have torque marker.  | THICKNESS (mm)<br>I <u>0</u><br>II <u>0</u><br>III <u>0</u><br>IV <u>0</u>  | ✓                      |                   | MOR<br>22/03/24 |
| 13  |   | Pivot fixation  | 1- M20 x 90 screws with application of torque according to PRA.FT1140.04 / 05   | ✓                      |                   | MOR<br>22/03/24 |
| 14  |  | FOR TC CARS<br>F= Height of the center of Automatic coupler<br>F = 895mm (+5 / -10mm)<br>(Using leveled rail)                                       | TC CAR #1 = _____ mm  |                        |                   | N/A             |
| 15  |  | FOR TC CARS<br>Height of Eurobalise Antenna = 205mm (+/-10mm)<br>(Using leveled rail)   | TC CAR #1 = _____ mm  |                        |                   | N/A             |
| 16  |  | Check pantograph piping air tightness.<br>Test performance according to VII PRA.FT1140.17.  | The test was performed and no leak was observed.<br>-Roof piping connection fittings.<br>-Room piping connection fittings (Roof arch and door blinning) | ✓                      |                   | MOR<br>22/03/24 |
| 17  |  | Pantograph does not come in contact with the higher height gauge when passing through.  | No Contact with Pantograph and Gauge -GO<br>Contact with Pantograph and Gauge - NO GO   | ✓                      |                   | MOR<br>22/03/24 |
| 18  |  | Car does not come into contact with the gauge.  | No Contact with Car and Gauge -GO<br>Contact with Car and Gauge - NO GO   | ✓                      |                   | MOR<br>22/03/24 |

  
 2024 -03- 2 2  
**CONTROLLED COPY**



# SELF INSPECTION INDUSTRIAL QUALITY

Rev:09

Date:

5/31/2022

Project:  
PRASA

SI.FT1140.52

## DRAFT TO MEASUREMENTS DURING LEVELLING (ALL UNITS MUST BE IN mm/bar/kg)

|                                    |                      | LEFT SIDE |   |   |   |     |     | RIGHT SIDE |     |   |   |   |   |
|------------------------------------|----------------------|-----------|---|---|---|-----|-----|------------|-----|---|---|---|---|
| DESCRIPTION                        | TOLERANCE            | 6         | 5 | 4 | 3 | 2   | 1   | 1          | 2   | 3 | 4 | 5 | 6 |
| AIR SPRING HEIGHT (EMPTY)          | N/A                  | A'II      |   |   |   |     |     |            |     |   |   |   |   |
| AIR SPRING HEIGHT (FULL)           | min 254<br>max 261   | AII       |   |   |   | 257 | 258 | 260        | 259 |   |   |   |   |
| FLOOR COVERING HEIGHT              | min 1096<br>max 1116 | EII       |   |   |   |     |     |            |     |   |   |   |   |
| AIR SPRING PRESSURE                | ≤ 0.3<br>(CI - CI)   | CII       |   |   |   | 302 | 305 | 290        | 291 |   |   |   |   |
| PRIMARY SUSPENSION                 | SEE TABLE (ONLY REF) | D3        |   |   |   |     |     |            |     |   |   |   |   |
| PRIMARY SUSPENSION                 | SEE TABLE (ONLY REF) | D4        |   |   |   |     |     |            |     |   |   |   |   |
| PIVOT VERTICAL GAP                 | min 25<br>max 32     | KII       |   |   |   |     |     |            |     |   |   |   |   |
| PIVOT LATERAL STOP GAPS DIFFERENCE | ≤ 4<br>(JI - JI)     | JII       |   |   |   |     |     |            |     |   |   |   |   |
| QTY OF TURNS OF LEVELLING ROD      | N/A                  | XII       |   |   |   |     |     |            |     |   |   |   |   |
| SHIMS OF ANTI-ROLL BAR             | N/A                  | YII       |   |   |   |     |     |            |     |   |   |   |   |
| DESCRIPTION                        | TOLERANCE            | 6         | 5 | 4 | 3 | 2   | 1   | 1          | 2   | 3 | 4 | 5 | 6 |
| AIR SPRING HEIGHT (EMPTY)          | N/A                  | A'III     |   |   |   |     |     |            |     |   |   |   |   |
| AIR SPRING HEIGHT (FULL)           | min 254<br>max 261   | AIII      |   |   |   | 257 | 258 | 261        | 259 |   |   |   |   |
| FLOOR COVERING HEIGHT              | min 1096<br>max 1116 | EIII      |   |   |   |     |     |            |     |   |   |   |   |
| AIR SPRING PRESSURE                | ≤ 0.3<br>(OI - OI)   | CIII      |   |   |   | 273 | 282 | 280        | 276 |   |   |   |   |
| PRIMARY SUSPENSION                 | SEE TABLE (ONLY REF) | D5        |   |   |   |     |     |            |     |   |   |   |   |
| PRIMARY SUSPENSION                 | SEE TABLE (ONLY REF) | D6        |   |   |   |     |     |            |     |   |   |   |   |
| PIVOT VERTICAL GAP                 | min 25<br>max 32     | KIII      |   |   |   |     |     |            |     |   |   |   |   |
| PIVOT LATERAL STOP GAPS DIFFERENCE | ≤ 4<br>(JI - JI)     | JIII      |   |   |   |     |     |            |     |   |   |   |   |
| QTY OF TURNS OF LEVELLING ROD      | N/A                  | XIII      |   |   |   |     |     |            |     |   |   |   |   |
| SHIMS OF ANTI-ROLL BAR             | N/A                  | YIII      |   |   |   |     |     |            |     |   |   |   |   |

COMPARE EACH TENTATIVE WITH THE TOLERANCE AND IDENTIFY EACH MEASURE AS BELOW



|      |       |        |
|------|-------|--------|
| GOOD | LOWER | HIGHER |
| ✓    | ↓     | ↑      |

WEIGHT  
COMPENSATION

|           |  |
|-----------|--|
| EQUIPMENT |  |
| WEIGHT    |  |
| EQUIPMENT |  |
| WEIGHT    |  |

SECONDARY MEASUREMENTS  
(ONLY TO CARS)

|                          |  |
|--------------------------|--|
| AUTOMATIC COUPLER HEIGHT |  |
| ANTENNA HEIGHT           |  |

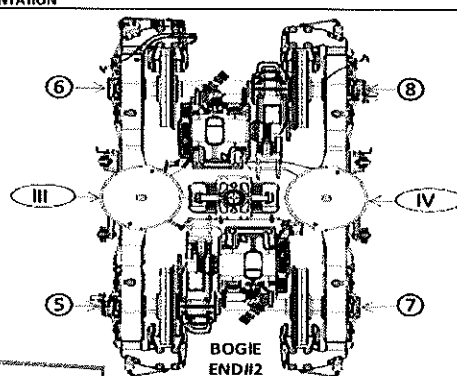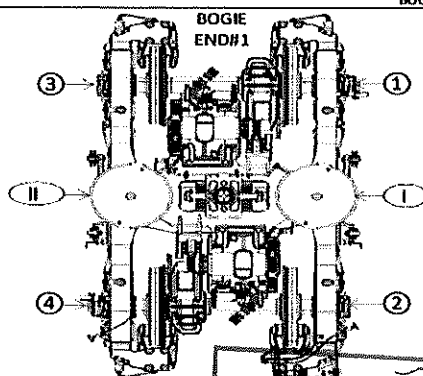

GIBELQ

2024 -03- 2 2

CONTROLLED COPY



# SELF INSPECTION INDUSTRIAL QUALITY

Rev:09

Date:

5/31/2022

Projet:  
PRASA



SI.FT1140.52

## DRAFT TO MEASUREMENTS DURING LEVELLING (ALL UNITS MUST BE IN mm/bar/kg)

| DESCRIPTION                        | TOLERANCE            | END#1     |   |   |   |   |   |            |   |   |   |   |   | END#2     |   |   |   |   |   |
|------------------------------------|----------------------|-----------|---|---|---|---|---|------------|---|---|---|---|---|-----------|---|---|---|---|---|
|                                    |                      | LEFT SIDE |   |   |   |   |   | RIGHT SIDE |   |   |   |   |   | LEFT SIDE |   |   |   |   |   |
|                                    |                      | 6         | 5 | 4 | 3 | 2 | 1 | 1          | 2 | 3 | 4 | 5 | 6 | 6         | 5 | 4 | 3 | 2 | 1 |
| AIR SPRING HEIGHT (EMPTY)          | N/A                  | A'II      |   |   |   |   |   |            |   |   |   |   |   | A'IV      |   |   |   |   |   |
| AIR SPRING HEIGHT (FULL)           | min 254<br>max 261   | AII       |   |   |   |   |   |            |   |   |   |   |   | AIV       |   |   |   |   |   |
| FLOOR COVERING HEIGHT              | min 1096<br>max 1116 | EII       |   |   |   |   |   |            |   |   |   |   |   | EIV       |   |   |   |   |   |
| AIR SPRING PRESSURE                | ≤ 0.3<br>(QI - CI)   | CII       |   |   |   |   |   |            |   |   |   |   |   | CIV       |   |   |   |   |   |
| PRIMARY SUSPENSION                 | SEE TABLE (ONLY REF) | D3        |   |   |   |   |   |            |   |   |   |   |   | D7        |   |   |   |   |   |
| PRIMARY SUSPENSION                 | SEE TABLE (ONLY REF) | D4        |   |   |   |   |   |            |   |   |   |   |   | D8        |   |   |   |   |   |
| PIVOT VERTICAL GAP                 | min 25<br>max 32     | KII       |   |   |   |   |   |            |   |   |   |   |   | KIV       |   |   |   |   |   |
| PIVOT LATERAL STOP GAPS DIFFERENCE | ≤ 4<br>(AI - AJ)     | JII       |   |   |   |   |   |            |   |   |   |   |   | JIV       |   |   |   |   |   |
| QTY OF TURNS OF LEVELLING ROD      | N/A                  | XII       |   |   |   |   |   |            |   |   |   |   |   | XIV       |   |   |   |   |   |
| SHIMS OF ANTI-ROLL BAR             | N/A                  | YII       |   |   |   |   |   |            |   |   |   |   |   | YIV       |   |   |   |   |   |
| AIR SPRING HEIGHT (EMPTY)          | N/A                  | A'III     |   |   |   |   |   |            |   |   |   |   |   | A'IV      |   |   |   |   |   |
| AIR SPRING HEIGHT (FULL)           | min 254<br>max 261   | AIII      |   |   |   |   |   |            |   |   |   |   |   | AIV       |   |   |   |   |   |
| FLOOR COVERING HEIGHT              | min 1096<br>max 1116 | EIII      |   |   |   |   |   |            |   |   |   |   |   | EIV       |   |   |   |   |   |
| AIR SPRING PRESSURE                | ≤ 0.3<br>(QV - CIV)  | CIII      |   |   |   |   |   |            |   |   |   |   |   | CIV       |   |   |   |   |   |
| PRIMARY SUSPENSION                 | SEE TABLE (ONLY REF) | D5        |   |   |   |   |   |            |   |   |   |   |   | D7        |   |   |   |   |   |
| PRIMARY SUSPENSION                 | SEE TABLE (ONLY REF) | D6        |   |   |   |   |   |            |   |   |   |   |   | D8        |   |   |   |   |   |
| PIVOT VERTICAL GAP                 | min 25<br>max 32     | KIII      |   |   |   |   |   |            |   |   |   |   |   | KIV       |   |   |   |   |   |
| PIVOT LATERAL STOP GAPS DIFFERENCE | ≤ 4<br>(AV - AB)     | JIII      |   |   |   |   |   |            |   |   |   |   |   | JIV       |   |   |   |   |   |
| QTY OF TURNS OF LEVELLING ROD      | N/A                  | XIII      |   |   |   |   |   |            |   |   |   |   |   | XIV       |   |   |   |   |   |
| SHIMS OF ANTI-ROLL BAR             | N/A                  | YIII      |   |   |   |   |   |            |   |   |   |   |   | YIV       |   |   |   |   |   |

COMPARE EACH TENTATIVE WITH THE TOLERANCE AND IDENTIFY EACH MEASURE AS BELOW

|                                       |       |        |
|---------------------------------------|-------|--------|
| GOOD                                  | LOWER | HIGHER |
| ✓                                     | ↓     | ↑      |
| WEIGHT COMPENSATION                   |       |        |
| EQUIPMENT                             |       |        |
| WEIGHT                                |       |        |
| EQUIPMENT                             |       |        |
| WEIGHT                                |       |        |
| SECONDARY MEASUREMENTS (ONLY TC CARS) |       |        |
| AUTOMATIC COUPLER HEIGHT              |       |        |
| ANTENNA HEIGHT                        |       |        |

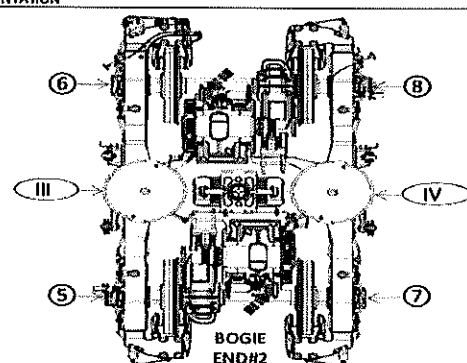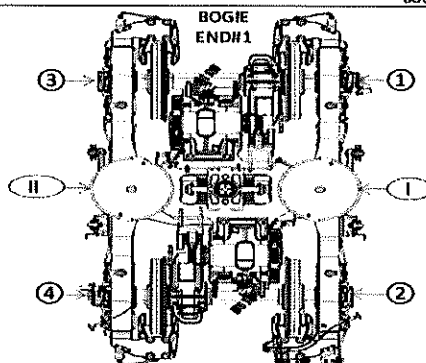

GIBELQ

2024 -03- 2 2

CONTROLLED COPY



# SELF INSPECTION INDUSTRIAL QUALITY

Rev:09

Date:

5/31/2022

Projeto:  
PRASA

SI.FT1140.52


Table 1 - Reference Values and Measurement Tolerances for the Car Levelling.

| ITEM                                   | THEORETICAL VALUES                 |                                    |                                    |                                    |                                    |                                    |                                    |                                    |                                    |                                    |                                    |                                    |                                    |                                    |
|--|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|------------------------------------|
|  | TCL CAR                            |                                    | M4 CAR                             |                                    | M1 CAR                             |                                    | M2 CAR                             |                                    | M3 CAR                             |                                    | TCL CAR                            |                                    |                                    |                                    |
|  | TBext                              | TBint                              | MB1                                | MB2                                | MB1                                | MB2                                | MB1                                | MB2                                | MB1                                | MB2                                | TBext                              | TBint                              | MB1                                | MB2                                |
| Pivot lateral stop gap difference [mm] | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                | ≤ 4                                |
| Air Spring height [mm]                 | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    | 255 <sup>+4</sup> <sub>-3</sub>    |
| Air spring pressure at AWD [Bar]       | 3,76                               | 2,82                               | 2,87                               | 2,83                               | 3,02                               | 2,91                               | 3,07                               | 2,85                               | 2,83                               | 2,87                               | 2,83                               | 2,83                               | 2,87                               | 3,76                               |
|  | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             | (Ref.)                             |
|  | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           | 0,3 Min.                           |
| Primary Suspension gaps [mm]           | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     | 35 <sup>+2</sup> <sub>-3</sub>     |
|  | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    | D <sub>12</sub> -D <sub>3</sub>    |
|  | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    | D <sub>12</sub> -D <sub>4</sub>    |
|  | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    | D <sub>12</sub> -D <sub>5</sub>    |
| Carbody Floor height [mm]              | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> | 1106 <sup>+25</sup> <sub>-15</sub> |
| Boiler height [mm]                     | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  | 850 <sup>+25</sup> <sub>-17</sub>  |
| Coupling End height [mm]               | 895 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         | 895 (Ref.)                         | 895 (Ref.)                         | 760 (Ref.)                         | 760 (Ref.)                         |
|  | Fig. 8                             | Fig. 9                             | Fig. 8                             | Fig. 9                             | Fig. 8                             | Fig. 9                             | Fig. 8                             | Fig. 9                             | Fig. 8                             | Fig. 9                             | Fig. 8                             | Fig. 9                             | Fig. 8                             | Fig. 9                             |
| Pivot Vertical gap [mm]                | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    | 30 <sup>+25</sup> <sub>-5</sub>    |

GIBELO

2024 - 03 - 22

CONTROLLED COPY

|   |   |           |                   |              |
|---|---|-----------|-------------------|--------------|
|  | <h1>SELF INSPECTION<br/>INDUSTRIAL QUALITY</h1> | Rev:09    | Project:<br>PRASA | SI.FT1140.52 |
|   |   | Date:     |                   |              |
|   |   | 5/31/2022 |                   |              |

Leveling report from Production (Final measurements after Levelling and Weighting fine)

References for secondary suspension empty

A'n Air spring height empty

References for secondary suspension full


An Air spring height  
 Bn Difference between measurement A'n and An  
 En Floor covering height  
 Cn Air spring pressure  
 Dn Primary suspension  
 Kn Pivot Vertical gap  
 Jn Pivot Lateral stop gaps difference

| Item                | Reference [mm]   | END#1        |           | END#2           |            |
|---------------------|------------------|--------------|-----------|-----------------|------------|
|                     |                  | Right Side   | Left Side | Left Side       | Right Side |
| A'n                 | N/A              | A'i 240      | A'ii 241  | A'iii 240       | A'iv 240   |
| An                  | 254 to 261       | Ai 259       | Aii 257   | Aiii 257        | Aiv 259    |
| Bn = An - A'n       | N/A              | Bi 19        | Bii 16    | Biii 17         | Biv 19     |
| En                  | 1106 ±10 mm      | Ei 1115      | Eii 1110  | Eiii 1110       | Eiv 1114   |
| Item                | Reference [bar]  | END#1        |           | END#2           |            |
|                     |                  | Right Side   | Left Side | Left Side       | Right Side |
| Cn                  | Table 02 (*)     | Ci 2.91      | Cii 3.01  | Ciii 2.82       | Civ 2.76   |
| Cn - Cn+1           | Difference ≤ 0,3 | Ci - Cii 0,1 |           | Ciii - Civ 0,06 |            |
| Gauge serial number | N/A              | G1B05875     |           | G1B05875        |            |
| Item                | Reference [mm]   | END#1        |           | END#2           |            |
|                     |                  | Right Side   | Left Side | Left Side       | Right Side |
| Dn                  | Table 01 (*)     | D1 44.68     | D2 44.07  | D3 45.10        | D4 45.27   |
|                     |                  | D2 44.28     | D4 44.36  | D5 44.61        | D7 44.80   |
| Kn                  | 25 to 45         | Ki 28.24     |           | Kii 31.09       |            |
| Jn                  | Difference ≤ 4   | Ji 24.31     | Jii 26.29 | Jiii 25.10      | Jiv 25.72  |

(\*) Reference, only include values, Isn't approval criteria.

| Table 01<br>D Theoretical Values | TC1                             |                                 | M4                              |                                 | M1                              |                                 | M2                              |                                 | M3                              |                                 | TC2                             |                                 |
|----------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|---------------------------------|
|                                  | Tbex                            | TBin                            | Mb1                             | Mb1                             | Mb1                             | Mb2                             | Mb1                             | Mb1                             | Mb1                             | Mb1                             | TBin                            | Tbex                            |
| D=                               | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> | 35 <sup>+12</sup> <sub>-5</sub> |

| Table 02<br>C Theoretical Values | TC1  |      | M4   |      | M1   |      | M2   |      | M3   |      | TC2  |      |
|----------------------------------|------|------|------|------|------|------|------|------|------|------|------|------|
|                                  | Tbex | TBin | Mb1  | Mb1  | Mb1  | Mb2  | Mb1  | Mb1  | Mb1  | Mb1  | TBin | Tbex |
| C=                               | 3.76 | 2.82 | 2.87 | 2.83 | 3.02 | 2.91 | 3.07 | 2.85 | 2.83 | 2.87 | 2.83 | 3.76 |

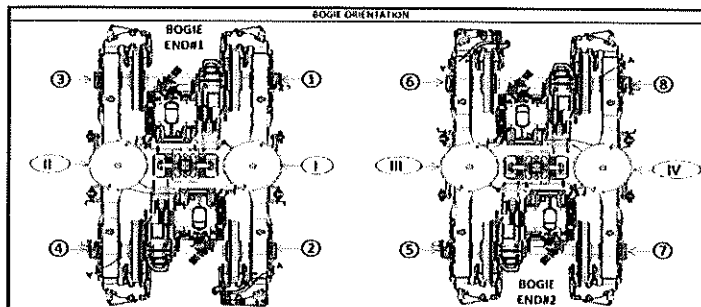

Weighting report from Test and Commissioning (Final measurements after Levelling and Weighting fine)







Gibela Rail Transport Consortium RF (Pty)  
Ltd  
2 Shesholaza Avenue  
Dunnetbar XT  
Ekurhuleni, 1590, South Africa  
Reception: +27 (0) 10 600 0651

|                      |  |
|----------------------|--|
| TRAIN SET 215        | REF: GIB000001672_10 PRASA WEIGHT BALANCE EN |
| PCOS WEIGHING REPORT |  |

| M2 | Balance across front and rear bogies |  | Front Bogie [Tons]     |  | Rear Bogie [Tons]       |  | Longitudinal Imbalance [%] |  | Criteria Longitudinal Imbalance $\leq 3\%$ |  |
|----|--------------------------------------|--|------------------------|--|-------------------------|--|----------------------------|--|--|--|
|    |                                      |  | 18.65                  |  | 17.97                   |  | 1.86%                      |  | PASS                                       |  |
|    | Weight Measured vs Predicted         |  | Weight Measured [Tons] |  | Weight Predicted [Tons] |  | Weight Difference [%]      |  | Tolerance [%]                              |  |
|    |                                      |  | 36.62                  |  | 37.06                   |  | 1.20%                      |  | 1.37%                                      |  |
|    |                                      |  |                        |  |                         |  |                            |  | Criteria Min/Diff/Max                      |  |
|    |                                      |  |                        |  |                         |  |                            |  | PASS                                       |  |

| Test Participants |         |            |            |
|-------------------|---------|------------|------------|
| Name              | Company | Department | Date       |
| Deshmukh          | GIBELA  | EOC        | 23/03/2024 |
| M.N.              |         |            |            |
